


ID	Task Name	Duration	Start	Finish	Jul 24, '18							Jul 31, '18							Aug 7, '18							Aug 14, '18							Aug 21, '18										
					S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W							
1	MOBILIZATION	3 days	Mon 7/24/17	Wed 7/26/17	■■■■■■■																																						
2	SET UP TEMP TRAFFIC CONTROL	1 day	Mon 7/24/17	Mon 7/24/17	■																																						
3	STAKE CLEARING LIMITS	1 day	Mon 7/24/17	Mon 7/24/17	■																																						
4	TEMP MOVE IRRIGATION LINES	2 days	Tue 7/25/17	Wed 7/26/17	■■																																						
5	DISCONNECT POWER TO PED LIGHTS	1 day	Tue 7/25/17	Tue 7/25/17	■																																						
6	DEMO PED LIGHTS	1 day	Tue 7/25/17	Tue 7/25/17	■																																						
7	INSTALL EROSION CONTROL (CB SOCKS)	1 day	Tue 7/25/17	Tue 7/25/17	■																																						
8	REMOVE RR TIES	2 days	Tue 7/25/17	Wed 7/26/17	■■																																						
9	CLEAR & GRUB	3 days	Tue 7/25/17	Thu 7/27/17	■■■																																						
10	INSTALL HVF	2 days	Wed 7/26/17	Thu 7/27/17	■■																																						
11	INSTALL WATTLE ALONG WEST SIDE	1 day	Thu 7/27/17	Thu 7/27/17	■																																						
12	DEMO CURB ON WEST SIDE 3RD	1 day	Thu 7/27/17	Thu 7/27/17	■																																						
13	SURVEY STORM	1 day	Thu 7/27/17	Thu 7/27/17	■																																						
14	POT HOLE EXISTING UTILITIES	2 days	Mon 7/31/17	Tue 8/1/17								■■																															
15	INSTALL STORM WEST SIDE OF 3RD	8 days	Mon 7/31/17	Thu 8/10/17								■■■■■■■																															
16	INSTALL STORM ON STATE ST	2 days	Mon 7/31/17	Tue 8/1/17								■■																															
17	BOLT WATER FITTINGS TOGETHER	2 days	Wed 8/2/17	Thu 8/3/17															■■																								
18	INSTALL SEWER STUB (FA)	1 day	Mon 8/7/17	Mon 8/7/17																						■																	
19	INSTALL NEW WATER MAIN	5 days	Mon 8/14/17	Mon 8/21/17																						■■■■■																	
20	BUILD BLOCK WALL	4 days	Mon 8/14/17	Thu 8/17/17																						■■■■																	
21	TEST & FLUSH NEW WATER MAIN	2 days	Tue 8/22/17	Wed 8/23/17																													■■										
22	INSTALL STORM XINGS ON 3RD	2 days	Tue 8/22/17	Wed 8/23/17																													■■										
23	PHASE 2 WATER TIE IN S. END	1 day	Thu 8/24/17	Thu 8/24/17																													■										
24	DEMO EXISTING CURBS & SIDEWALKS	1 day	Mon 8/28/17	Mon 8/28/17																													■										
25	INSTALL NEW SERVICES	1 day	Mon 8/28/17	Mon 8/28/17																													■										
26	PHASE 1 WATER TIE IN N. END	1 day	Tue 8/29/17	Tue 8/29/17																													■										
27	INSTALL ROOT BARRIER	2 days	Tue 8/29/17	Wed 8/30/17																													■■										
28	PHASE 3 WATER TIE IN S. END	1 day	Wed 8/30/17	Wed 8/30/17																													■										
29	PHASE 1 WATER TIE IN S. END	1 day	Thu 8/31/17	Thu 8/31/17																													■										
30	POWER TRENCHING & SET NEW LIGHTS	3 days	Tue 9/5/17	Thu 9/7/17																													■■■										
31	GRADE FOR NEW CURBS	2 days	Tue 9/5/17	Wed 9/6/17																													■■										
32	PHASE 2 WATER TIE IN N. END	1 day	Tue 9/5/17	Tue 9/5/17																													■										
33	HOT TAP NEW FIRE HYD	1 day	Wed 9/6/17	Wed 9/6/17																													■										
34	INSTALL NEW FIRE HYD'S	1 day	Wed 9/6/17	Wed 9/6/17																													■										
35	POUR NEW CURBS	3 days	Thu 9/7/17	Tue 9/12/17																													■■■										
36	GRADE FOR SIDEWALKS	2 days	Wed 9/13/17	Thu 9/14/17																													■■										
37	POUR NEW SIDE WALKS	3 days	Thu 9/14/17	Tue 9/19/17																													■■■										
38	GRIND EXISTING ASPHALT	1 day	Wed 9/20/17	Wed 9/20/17																													■										
39	GRADE FOR ROAD SUB GRADE	1 day	Wed 9/20/17	Wed 9/20/17																													■										
40	FDR EXISTING ROADS	1 day	Thu 9/21/17	Thu 9/21/17																													■										
41	GRADE FOR ASPHALT	2 days	Thu 9/21/17	Mon 9/25/17																													■■										
42	ADJUST IRON	1 day	Thu 9/21/17	Thu 9/21/17																													■										
43	ASPHALT ROADS	2 days	Tue 9/26/17	Wed 9/27/17																													■■										
44	STRIP ROADS	1 day	Thu 9/28/17	Thu 9/28/17																													■										
45	INSTALL NEW SIGNS	1 day	Thu 9/28/17	Thu 9/28/17																													■										
46	NEW LANDSCAPING	4 days	Thu 9/28/17	Wed 10/4/17																													■■■■										
47	INSTALL NEW IRRIGATION SYSTEM	2 days	Wed 10/4/17	Thu 10/5/17																													■■										
48	TOP SOIL & SEED	2 days	Mon 10/9/17	Tue 10/10/17																													■■										
49	WOOD CHIP MULCH	1 day	Mon 10/9/17	Mon 10/9/17																													■										
50	REMOVE EROSION CONTROL	1 day	Wed 10/11/17	Wed 10/11/17																													■										
51	CLEAN UP & DEMOB	2 days	Wed 10/11/17	Thu 10/12/17																													■■										

Project: SCHEDULE Date: Thu 7/27/17	Task	Milestone	Rolling Up Task	Rolling Up Progress	External Tasks	Group By Summary
	Progress	Summary	Rolling Up Milestone	Split	Project Summary	Deadline

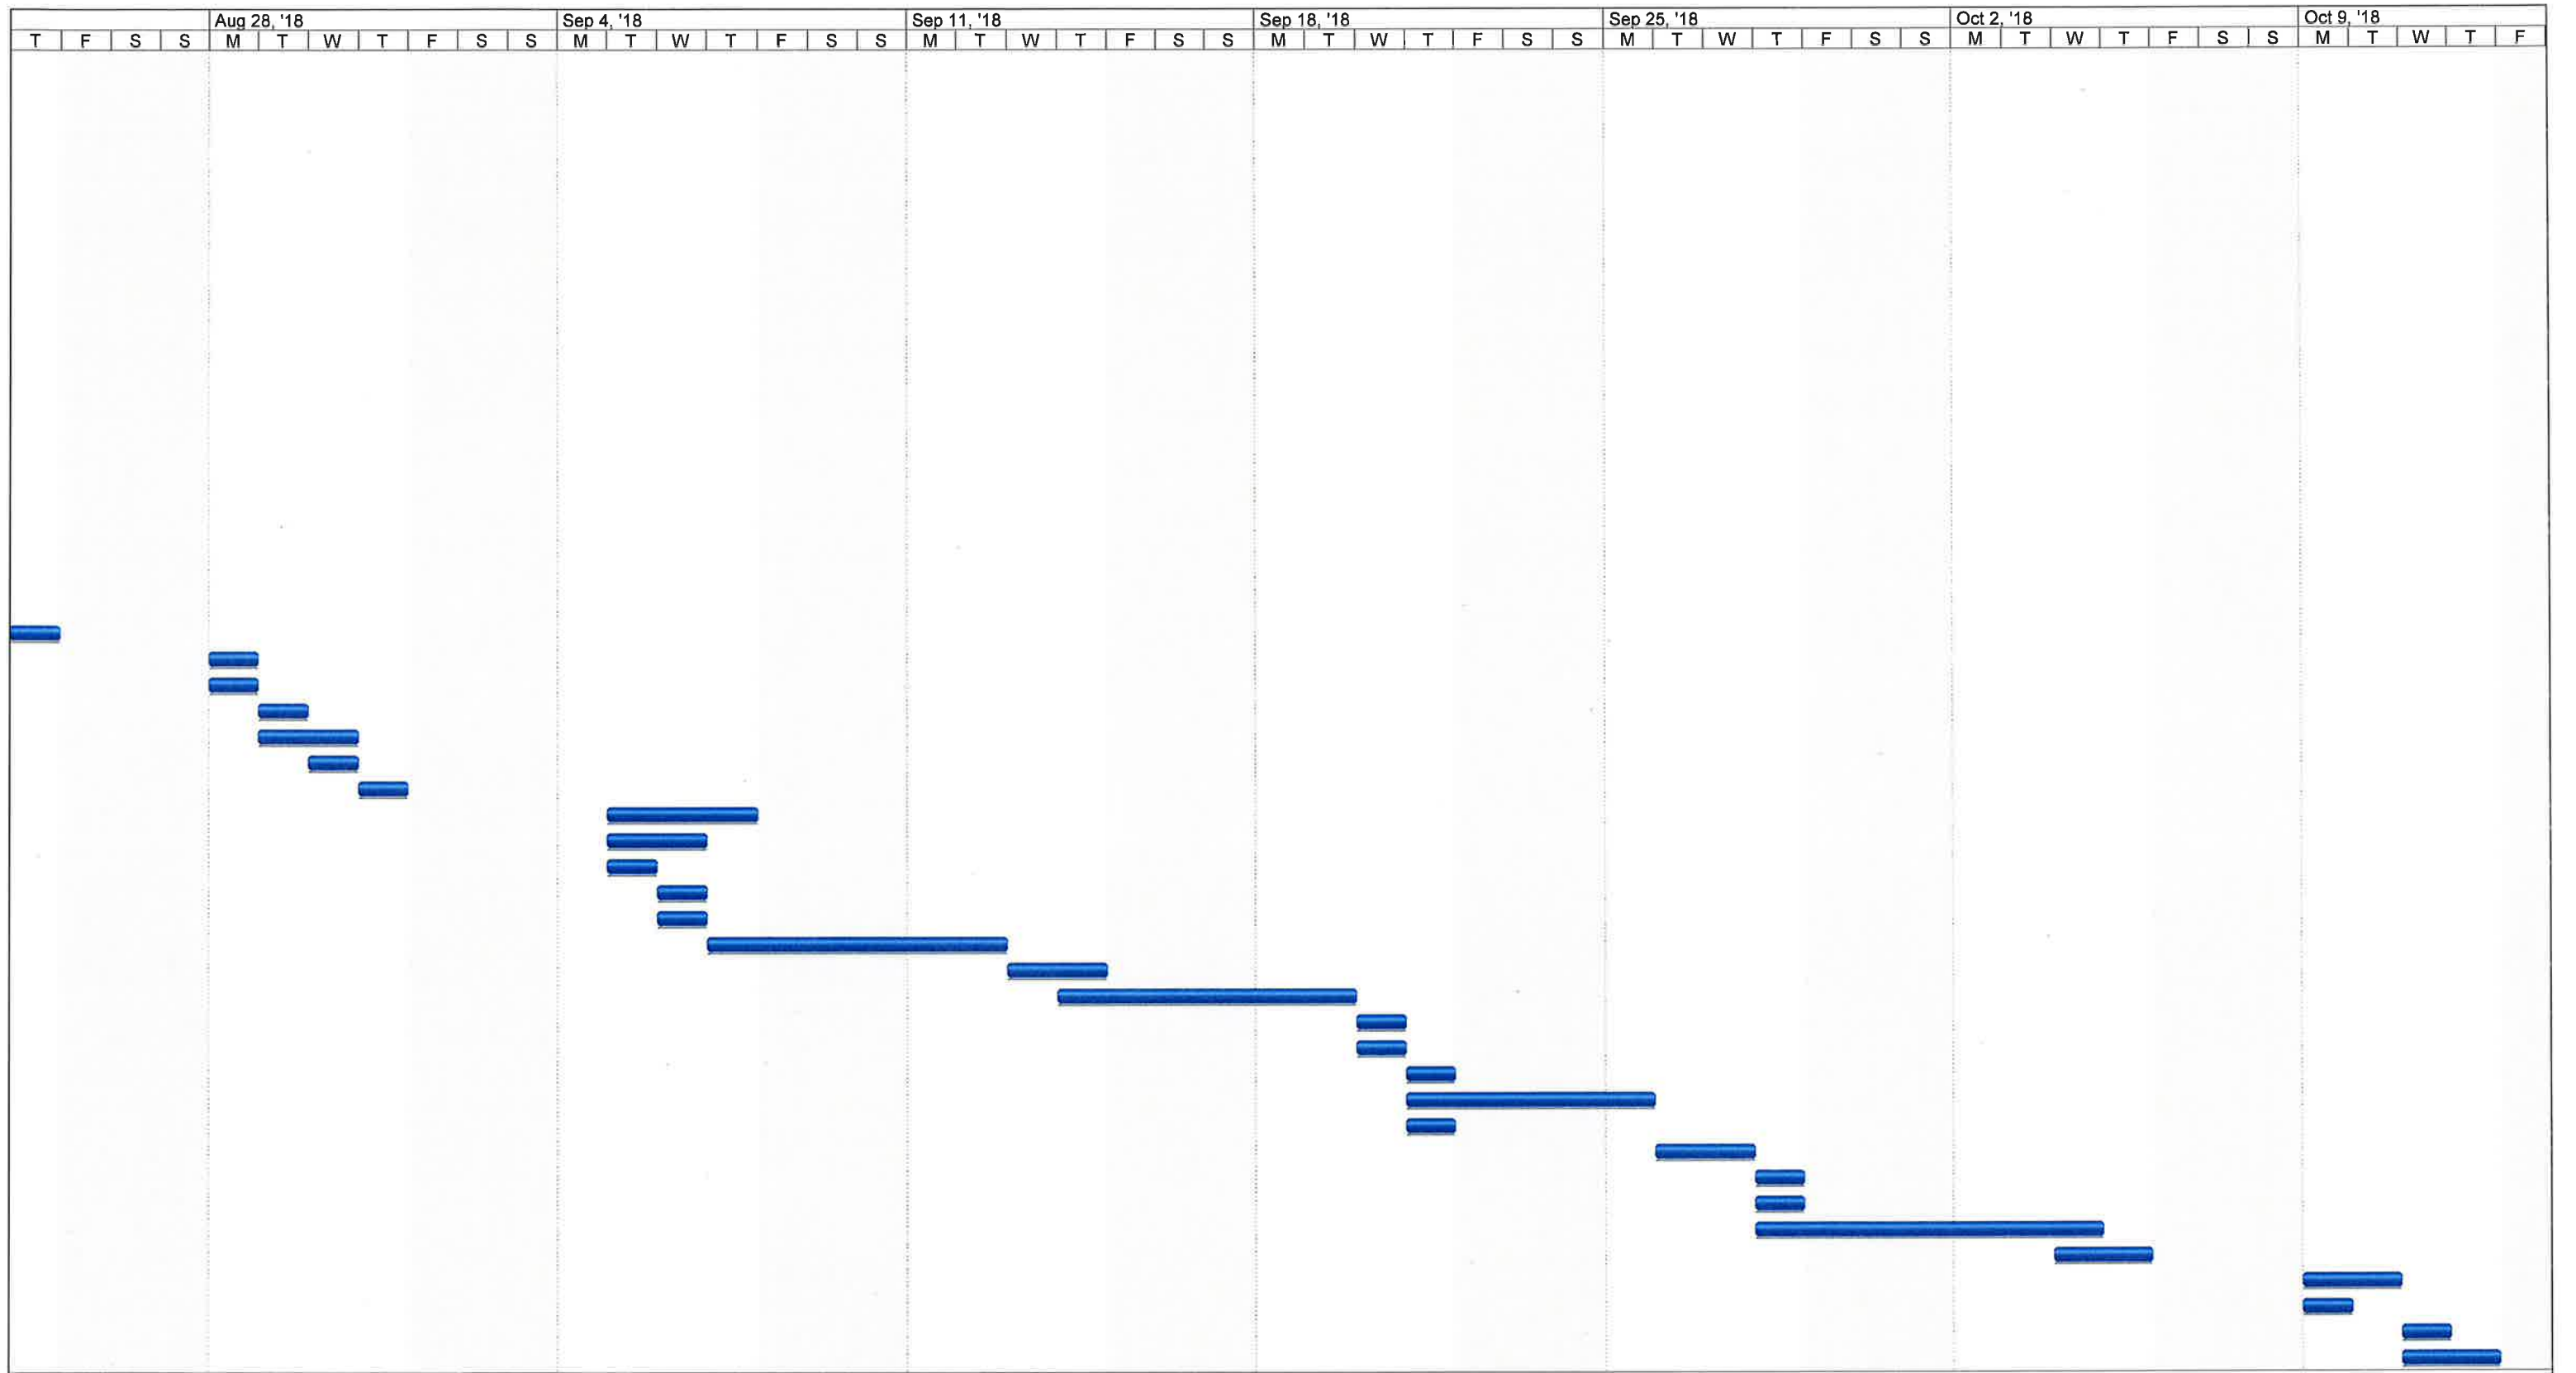

Project: SCHEDULE
Date: Thu 7/27/17

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
Progress		Summary		Rolled Up Milestone		Split		Project Summary		Deadline	
